



NCCC CONSTRUCTION SCHEDULE



Project: NCCC Learning Commons
Date: 2/27/17

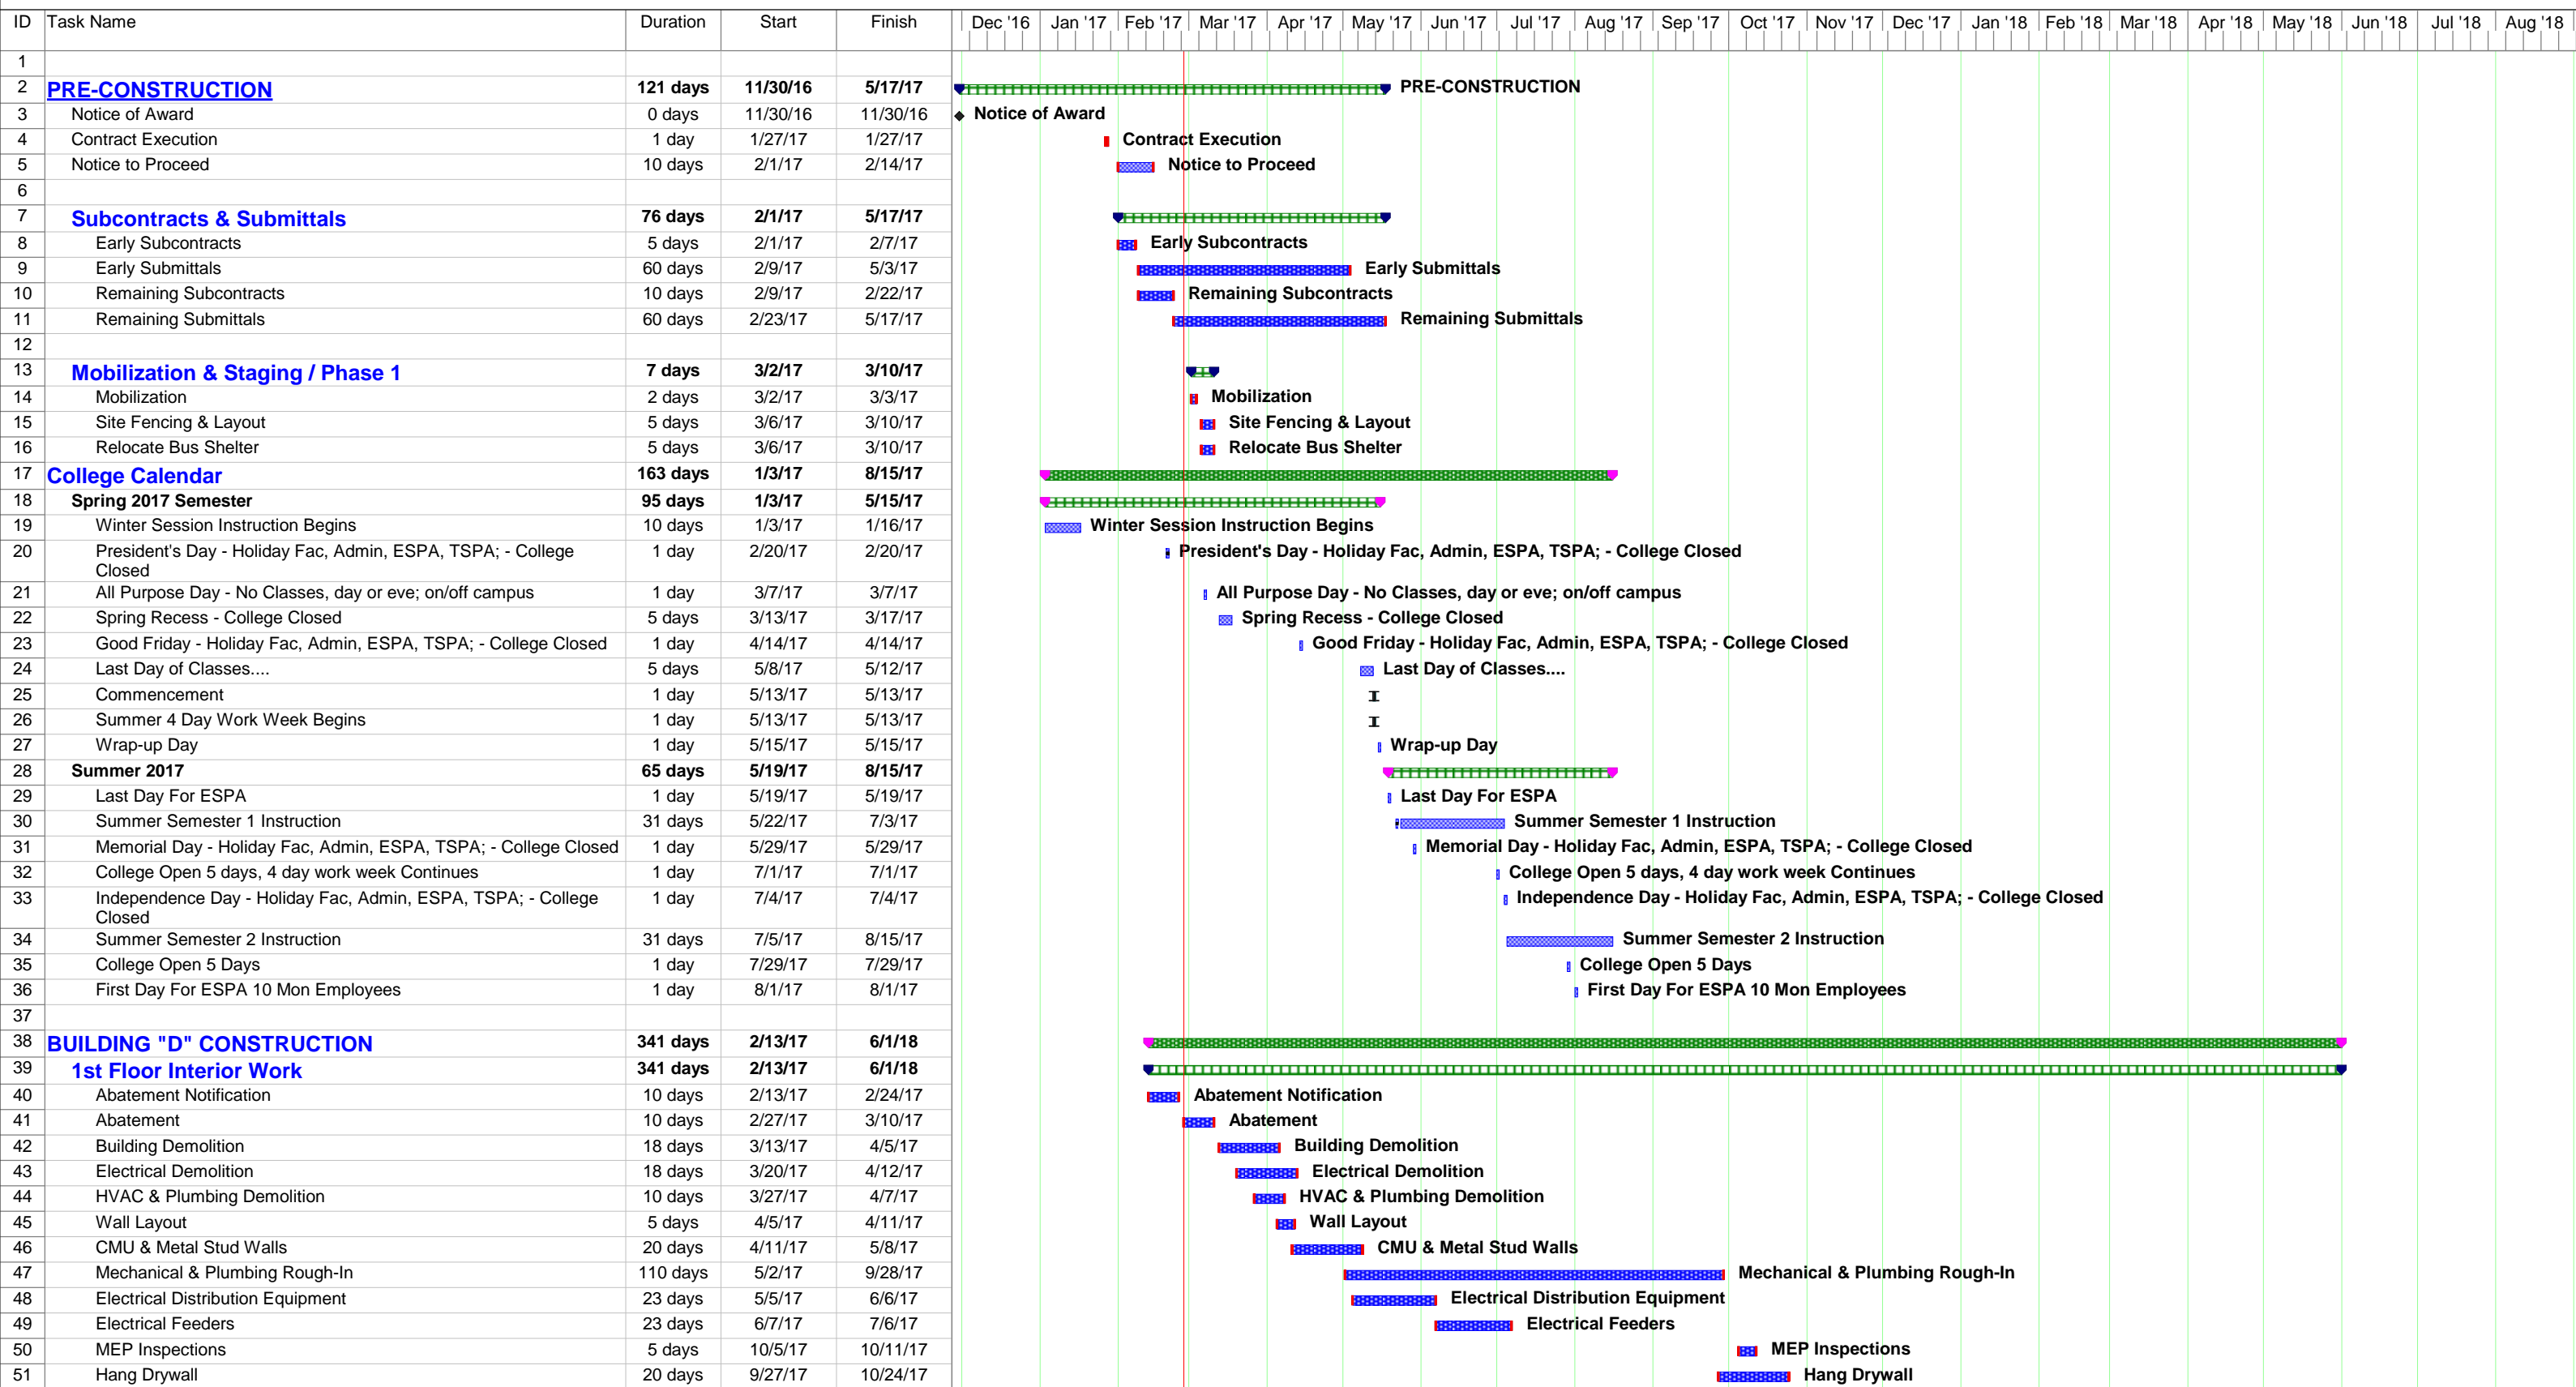


Task		Project Summary		Inactive Summary		Manual Summary		External Milestone
Split		External Tasks		Manual Task		Start-only		Progress
Milestone		External Milestone		Duration-only		Finish-only		Deadline
Summary		Inactive Milestone		Manual Summary Rollup		External Tasks		

NCCC CONSTRUCTION SCHEDULE

ID	Task Name	Duration	Start	Finish	Dec '16	Jan '17	Feb '17	Mar '17	Apr '17	May '17	Jun '17	Jul '17	Aug '17	Sep '17	Oct '17	Nov '17	Dec '17	Jan '18	Feb '18	Mar '18	Apr '18	May '18	Jun '18	Jul '18	Aug '18
52	Finish Drywall	10 days	10/24/17	11/6/17																					
53	Prime & First Coat	15 days	11/6/17	11/24/17																					
54	Ceiling Grid	14 days	11/27/17	12/14/17																					
55	Lighting	68 days	12/8/17	3/13/18																					
56	Ceramic Tile	25 days	3/6/18	4/9/18																					
57	Final Painting	15 days	3/12/18	3/30/18																					
58	Flooring	20 days	3/29/18	4/25/18																					
59	Millwork	10 days	4/23/18	5/4/18																					
60	Commissioning, Start & Testing	5 days	4/25/18	5/1/18																					
61	Electrical Finishes	12 days	5/1/18	5/16/18																					
62	Ceiling Tile Install	10 days	4/27/18	5/10/18																					
63	Mechanical & Plumbing Finishes	3 days	4/30/18	5/2/18																					
64	Toilet Partitions & Accessories	5 days	5/1/18	5/7/18																					
65	Doors & Hardware	20 days	4/19/18	5/16/18																					
66	Substantial Completion	0 days	5/1/18	5/1/18																					
67	Final Completion	0 days	6/1/18	6/1/18																					
68																									
69	2nd Floor Interior Work	321 days	3/13/17	6/1/18																					
70	Abatement	10 days	3/13/17	3/24/17																					
71	Building Demolition	20 days	3/24/17	4/20/17																					
72	Electrical Demolition	14 days	3/30/17	4/18/17																					
73	HVAC & Plumbing Demolition	9 days	4/6/17	4/18/17																					
74	Wall Layout	5 days	4/21/17	4/27/17																					
75	CMU & Metal Stud Walls	10 days	4/27/17	5/10/17																					
76	Mechanical & Plumbing Rough-In	35 days	5/5/17	6/22/17																					
77	Electrical Distribution Equipment	18 days	5/10/17	6/2/17																					
78	Electrical Feeders	14 days	6/2/17	6/21/17																					
79	MEP Inspections	5 days	6/23/17	6/29/17																					
80	Hang Drywall	10 days	6/22/17	7/4/17																					
81	Finish Drywall	10 days	7/7/17	7/20/17																					
82	Prime & First Coat	10 days	7/19/17	7/31/17																					
83	Ceiling Grid	10 days	7/31/17	8/11/17																					
84	Lighting	53 days	8/11/17	10/24/17																					
85	Ceramic Tile	10 days	10/25/17	11/7/17																					
86	Final Painting	10 days	10/26/17	11/8/17																					
87	Flooring	16 days	11/8/17	11/29/17																					
88	Millwork	7 days	12/4/17	12/12/17																					
89	Commissioning, Start & Testing	5 days	12/4/17	12/8/17																					
90	Electrical Finishes	12 days	12/11/17	12/26/17																					
91	Ceiling Tile Install	5 days	12/8/17	12/14/17																					
92	Mechanical & Plumbing Finishes	5 days	12/11/17	12/15/17																					
93	Doors & Hardware	11 days	12/15/17	12/29/17																					
94	Substantial Completion	0 days	5/1/18	5/1/18																					
95	Final Completion	0 days	6/1/18	6/1/18																					
96																									
97	3rd Floor Interior Work	311 days	3/27/17	6/1/18																					
98	Abatement	5 days	3/27/17	3/31/17																					
99	Building Demolition	5 days	3/31/17	4/6/17																					
100	Electrical Demolition	5 days	4/3/17	4/7/17																					
101	HVAC & Plumbing Demolition	10 days	4/3/17	4/14/17																					
102	Wall Layout	1 day	4/7/17	4/7/17																					
103	Metal Stud Walls	5 days	4/10/17	4/14/17																					

Project: NCCC Learning Commons
Date: 2/27/17
























Task		Project Summary		Inactive Summary		Manual Summary		External Milestone
Split		External Tasks		Manual Task		Start-only		Progress
Milestone		External Milestone		Duration-only		Finish-only		Deadline
Summary		Inactive Milestone		Manual Summary Rollup		External Tasks		External Milestone

NCCC CONSTRUCTION SCHEDULE


ID	Task Name	Duration	Start	Finish	Dec '16	Jan '17	Feb '17	Mar '17	Apr '17	May '17	Jun '17	Jul '17	Aug '17	Sep '17	Oct '17	Nov '17	Dec '17	Jan '18	Feb '18	Mar '18	Apr '18	May '18	Jun '18	Jul '18	Aug '18
104	Mechanical & Plumbing Rough-In	15 days	4/17/17	5/5/17																					
105	Electrical Distribution Equipment	5 days	4/20/17	4/26/17																					
106	Electrical Feeders	5 days	4/26/17	5/2/17																					
107	MEP Inspections	2 days	5/8/17	5/9/17																					
108	Hang Drywall	5 days	5/10/17	5/16/17																					
109	Finish Drywall	5 days	5/17/17	5/23/17																					
110	Lighting	15 days	10/26/17	11/15/17																					
111	Electrical Finishes	5 days	12/27/17	1/2/18																					
112	Mechanical & Plumbing Finishes	5 days	12/18/17	12/22/17																					
113	Substantial Completion	0 days	5/1/18	5/1/18																					
114	Final Completion	0 days	6/1/18	6/1/18																					
115																									
116	4th Floor Interior Work	306 days	4/3/17	6/1/18																					
117	Abatement	7 days	4/3/17	4/11/17																					
118	Electrical Demolition	5 days	4/12/17	4/18/17																					
119	HVAC & Plumbing Demolition	5 days	4/19/17	4/25/17																					
120	Wall Layout	1 day	4/19/17	4/19/17																					
121	Metal Stud Walls	5 days	4/20/17	4/26/17																					
122	Mechanical & Plumbing Rough-In	15 days	4/27/17	5/17/17																					
123	Electrical Distribution Equipment	5 days	5/3/17	5/9/17																					
124	Electrical Feeders	5 days	5/10/17	5/16/17																					
125	MEP Inspections	2 days	5/17/17	5/18/17																					
126	Hang Drywall	5 days	5/19/17	5/25/17																					
127	Finish Drywall	5 days	5/26/17	6/1/17																					
128	Lighting	15 days	11/16/17	12/6/17																					
129	Electrical Finishes	5 days	12/8/17	12/14/17																					
130	Mechanical & Plumbing Finishes	5 days	12/7/17	12/13/17																					
131	Substantial Completion	0 days	5/1/18	5/1/18																					
132	Final Completion	0 days	6/1/18	6/1/18																					
133																									
134	Upper Mechanical Room	301 days	4/10/17	6/1/18																					
135	HVAC & Mechanical Demolition	5 days	4/10/17	4/14/17																					
136	Electrical Demolition	5 days	4/10/17	4/14/17																					
137	Wall Layout	1 day	4/17/17	4/17/17																					
138	Metal Stud Walls	5 days	4/18/17	4/24/17																					
139	Mechanical & Plumbing Rough-In	55 days	4/25/17	7/7/17																					
140	Electrical Distribution Equipment	10 days	6/20/17	7/1/17																					
141	Electrical Feeders	5 days	7/3/17	7/7/17																					
142	MEP Inspections	2 days	7/12/17	7/13/17																					
143	Lighting	1 day	12/11/17	12/11/17																					
144	Electrical Finishes	4 days	12/12/17	12/15/17																					
145	Mechanical & Plumbing Finishes	4 days	12/12/17	12/15/17																					
146	Substantial Completion	0 days	5/1/18	5/1/18																					
147	Final Completion	0 days	6/1/18	6/1/18																					
148																									
149	Exterior Work Building	287 days	4/28/17	6/1/18																					
150	West Side Concrete Column Repair	20 days	4/28/17	5/25/17																					
151	Paver Salvage & Roof Removal	15 days	5/10/17	5/30/17																					
152	New Roofing	30 days	6/1/17	7/11/17																					
153	Paint Exterior Surfaces	20 days	7/14/17	8/9/17																					
154	Abate / Remove Windows	15 days	8/11/17	8/31/17																					
155	New Windows	21 days	8/18/17	9/15/17																					

Project: NCCC Learning Commons
Date: 2/27/17




Task		Project Summary		Inactive Summary		Manual Summary		External Milestone		Progress
Split		External Tasks		Manual Task		Start-only		Finish-only		Deadline
Milestone		External Milestone		Duration-only		Manual Summary Rollup		External Tasks		External Milestone
Summary		Inactive Milestone		Manual Summary Rollup		External Tasks		External Milestone		External Milestone

NCCC CONSTRUCTION SCHEDULE

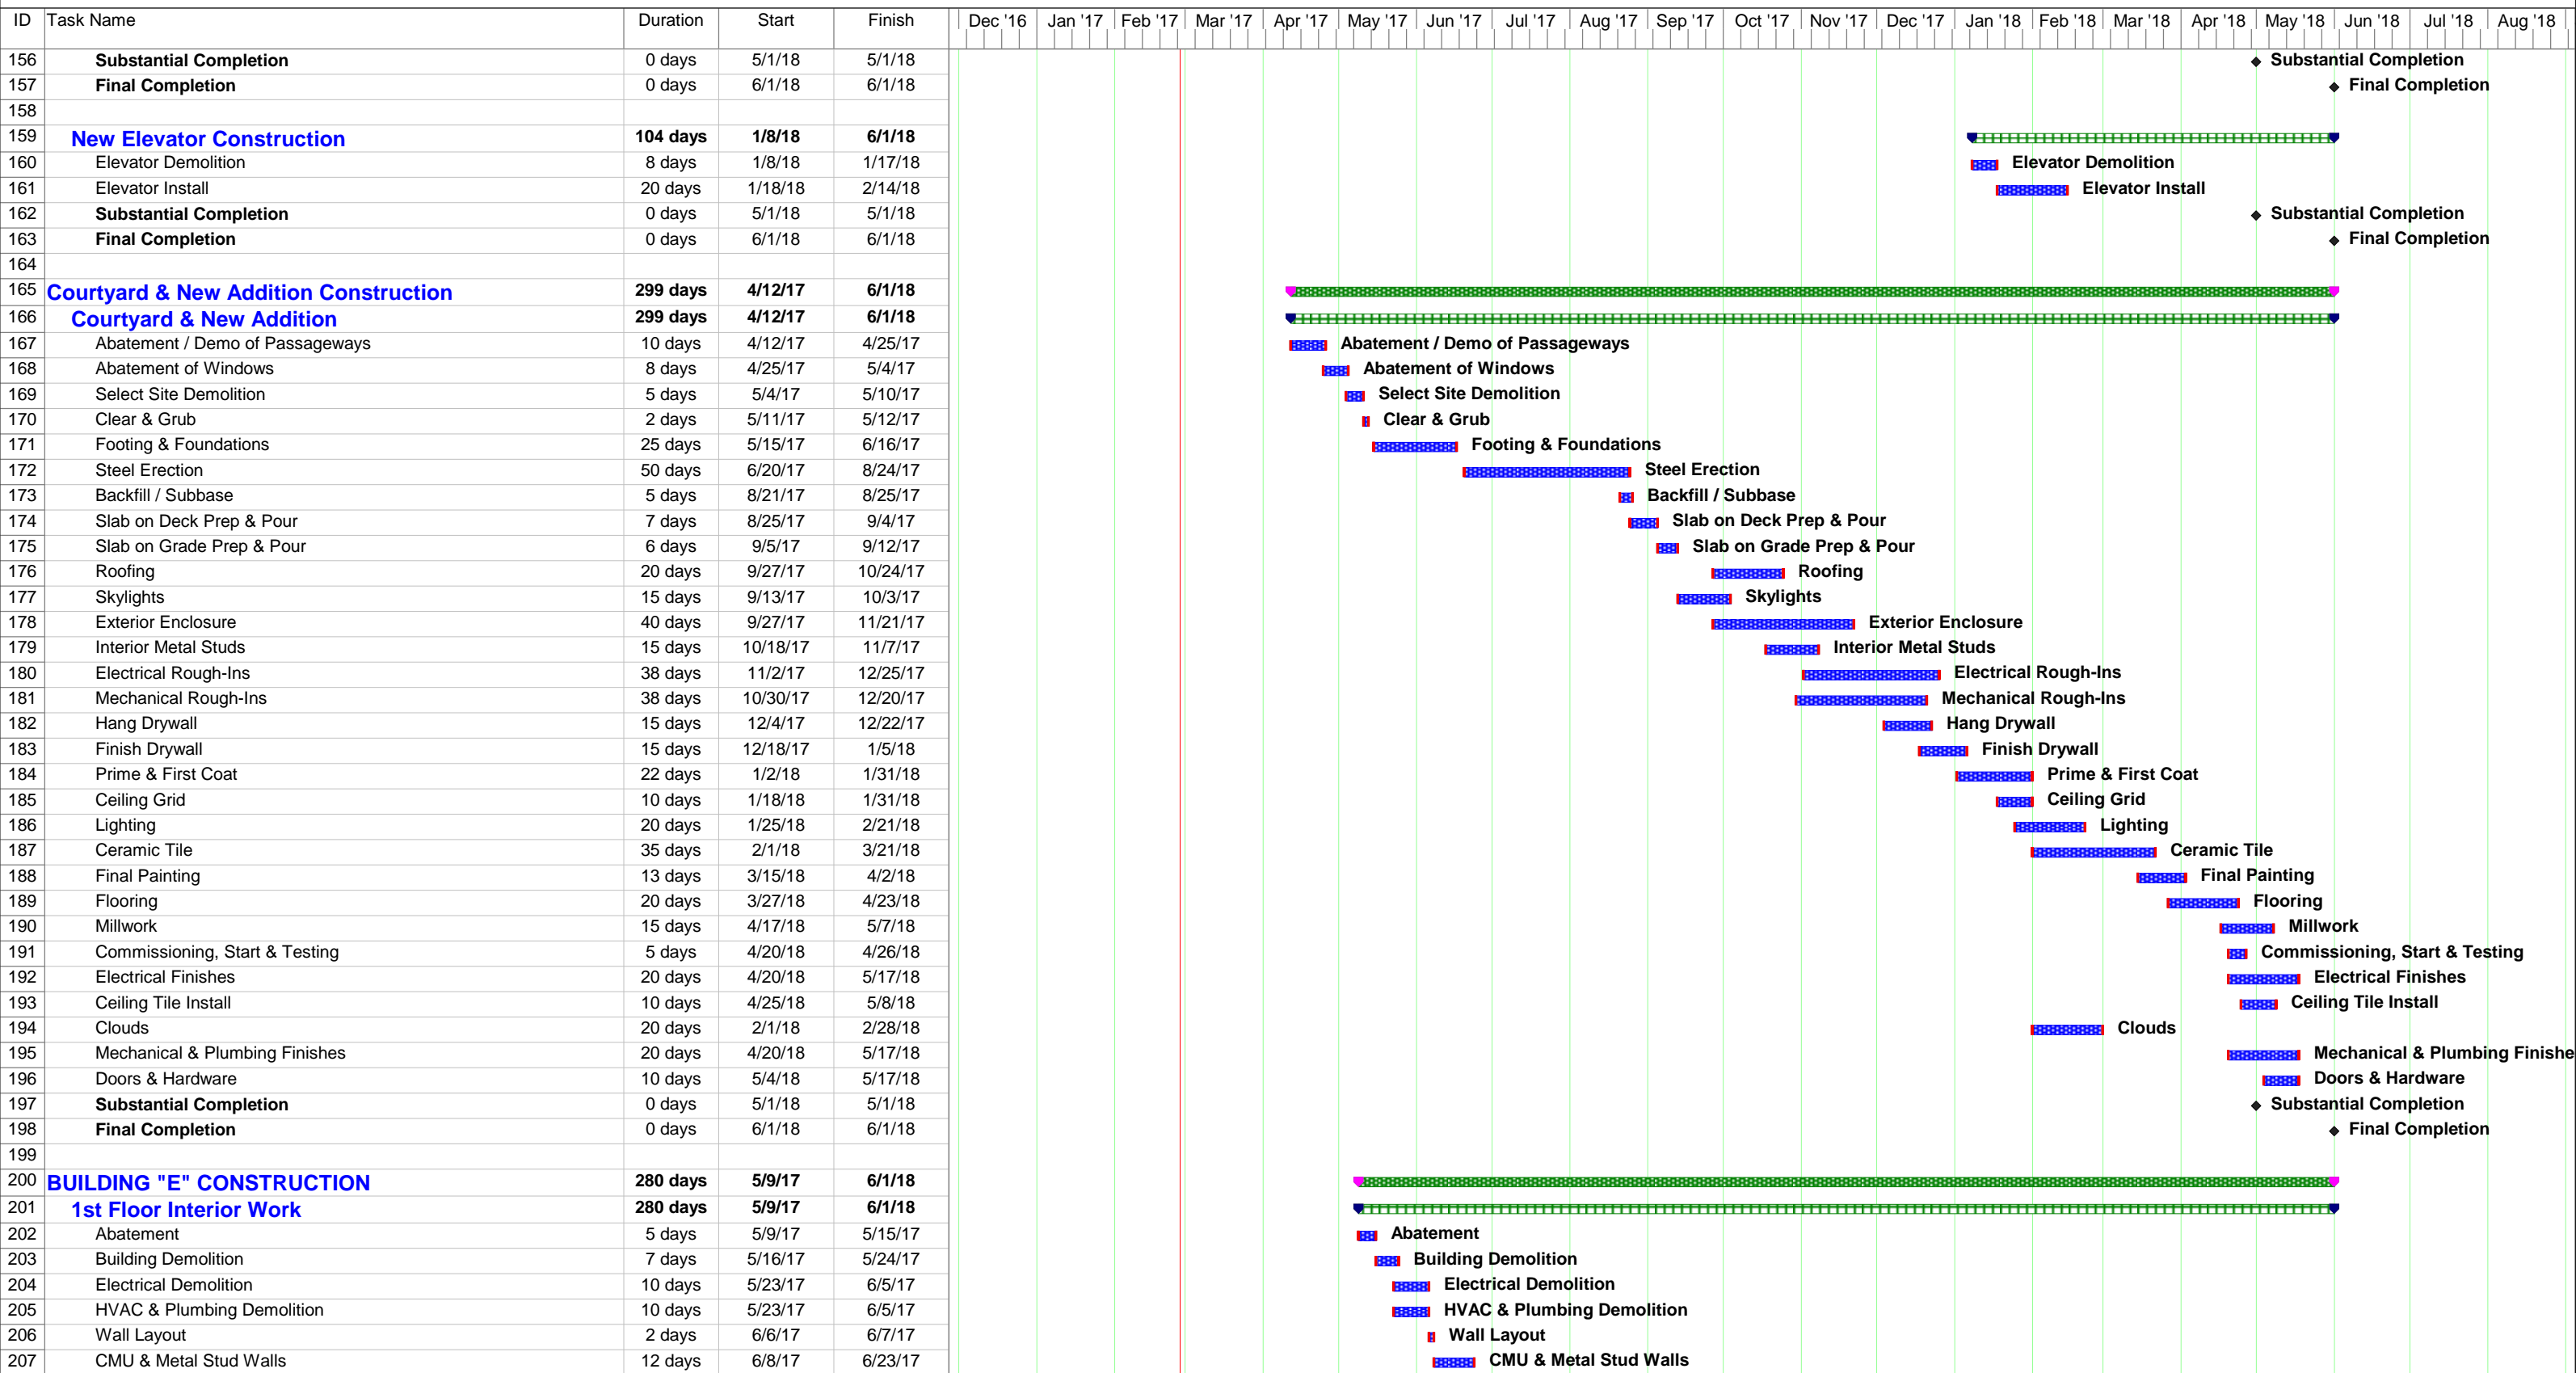

Project: NCCC Learning Commons
Date: 2/27/17






















Task		Project Summary		Inactive Summary		Manual Task		Start-only		Progress		Deadline
Split		External Tasks		Manual Task		Start-only		Finish-only		Deadline		External Milestone
Milestone		External Milestone		Manual Task		Start-only		Finish-only		Deadline		External Milestone
Summary		Inactive Milestone		Manual Task		Start-only		Finish-only		Deadline		External Milestone

NCCC CONSTRUCTION SCHEDULE

ID	Task Name	Duration	Start	Finish	Dec '16	Jan '17	Feb '17	Mar '17	Apr '17	May '17	Jun '17	Jul '17	Aug '17	Sep '17	Oct '17	Nov '17	Dec '17	Jan '18	Feb '18	Mar '18	Apr '18	May '18	Jun '18	Jul '18	Aug '18
208	Mechanical & Plumbing Rough-In	10 days	6/22/17	7/4/17																					
209	Electrical Distribution Equipment	10 days	6/22/17	7/4/17																					
210	Electrical Feeders	10 days	7/5/17	7/18/17																					
211	MEP Inspections	2 days	7/18/17	7/19/17																					
212	Hang Drywall	5 days	7/19/17	7/25/17																					
213	Finish Drywall	2 days	7/26/17	7/27/17																					
214	Prime & First Coat	6 days	7/27/17	8/2/17																					
215	Ceiling Grid	6 days	8/3/17	8/10/17																					
216	Lighting	10 days	8/9/17	8/22/17																					
217	Ceramic Tile	5 days	8/22/17	8/28/17																					
218	Final Painting	3 days	8/23/17	8/25/17																					
219	Flooring	5 days	8/25/17	8/31/17																					
220	Commissioning, Start & Testing	2 days	9/1/17	9/4/17																					
221	Electrical Finishes	10 days	8/31/17	9/13/17																					
222	Ceiling Tile Install	8 days	9/6/17	9/15/17																					
223	Toilet Partitions & Accessories	3 days	9/12/17	9/14/17																					
224	Mechanical & Plumbing Finishes	10 days	9/1/17	9/14/17																					
225	Doors & Hardware	8 days	9/14/17	9/25/17																					
226	Substantial Completion	0 days	5/1/18	5/1/18																					
227	Final Completion	0 days	6/1/18	6/1/18																					
228																									
229	2nd Floor Interior Work	275 days	5/16/17	6/1/18																					
230	Abatement	5 days	5/16/17	5/22/17																					
231	Building Demolition	7 days	5/23/17	5/31/17																					
232	Electrical Demolition	10 days	5/31/17	6/13/17																					
233	HVAC & Plumbing Demolition	10 days	5/31/17	6/13/17																					
234	Wall Layout	2 days	6/13/17	6/14/17																					
235	CMU & Metal Stud Walls	12 days	6/15/17	6/30/17																					
236	Mechanical & Plumbing Rough-In	10 days	6/29/17	7/11/17																					
237	Electrical Distribution Equipment	10 days	7/14/17	7/27/17																					
238	Electrical Feeders	10 days	7/27/17	8/8/17																					
239	MEP Inspections	2 days	8/9/17	8/10/17																					
240	Hang Drywall	5 days	8/10/17	8/16/17																					
241	Finish Drywall	2 days	8/16/17	8/17/17																					
242	Prime & First Coat	6 days	8/21/17	8/28/17																					
243	Ceiling Grid	5 days	8/28/17	9/1/17																					
244	Lighting	10 days	8/31/17	9/13/17																					
245	Ceramic Tile	5 days	9/14/17	9/20/17																					
246	Final Painting	3 days	9/15/17	9/19/17																					
247	Flooring	5 days	9/19/17	9/25/17																					
248	Commissioning, Start & Testing	2 days	9/26/17	9/27/17																					
249	Electrical Finishes	10 days	9/25/17	10/6/17																					
250	Ceiling Tile Install	6 days	9/27/17	10/4/17																					
251	Mechanical & Plumbing Finishes	10 days	9/25/17	10/6/17																					
252	Doors & Hardware	8 days	10/5/17	10/16/17																					
253	Substantial Completion	0 days	5/1/18	5/1/18																					
254	Final Completion	0 days	6/1/18	6/1/18																					

Project: NCCC Learning Commons
Date: 2/27/17



Task		Project Summary		Inactive Summary		Manual Summary		External Milestone	
Split		External Tasks		Manual Task		Start-only		Progress	
Milestone		External Milestone		Duration-only		Finish-only		Deadline	
Summary		Inactive Milestone		Manual Summary Rollup		External Tasks	
